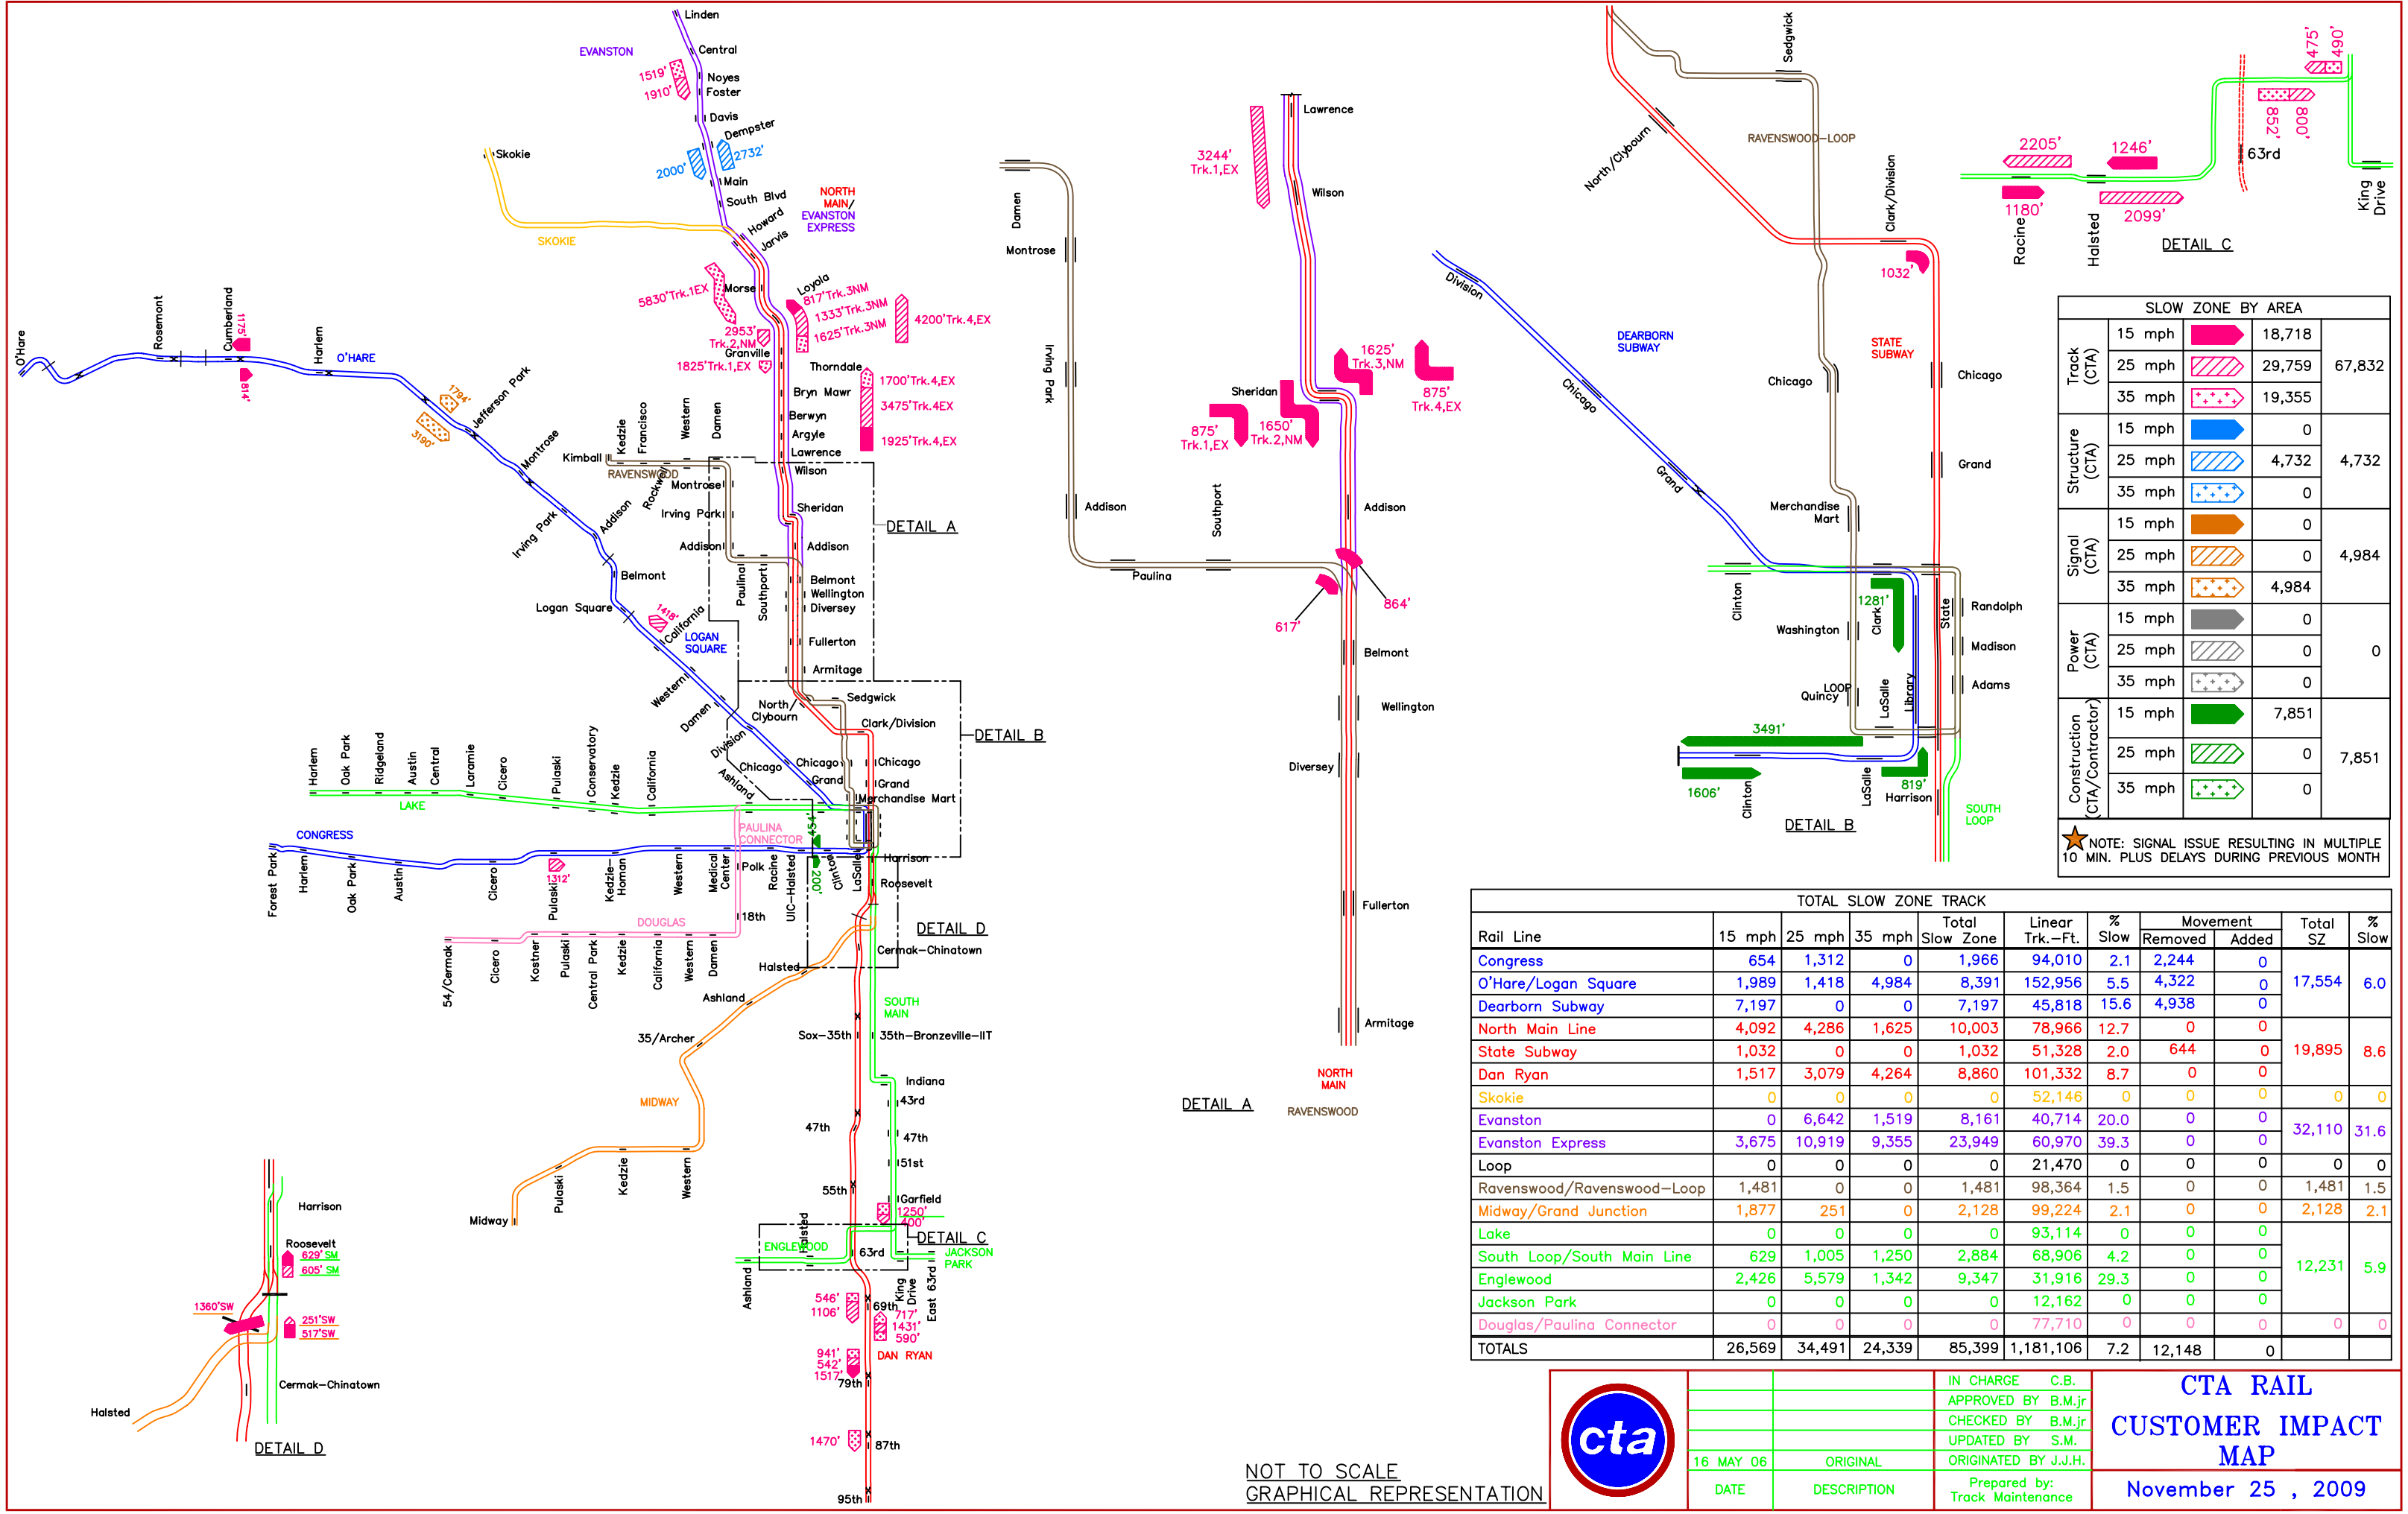

SLOW ZONE BY AREA				
Track (CTA)	15 mph		18,718	67,832
	25 mph		29,759	
	35 mph		19,355	
Structure (CTA)	15 mph		0	4,732
	25 mph		4,732	
	35 mph		0	
Signal (CTA)	15 mph		0	4,984
	25 mph		0	
	35 mph		4,984	
Power (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Construction (CTA/Contractor)	15 mph		7,851	7,851
	25 mph		0	
	35 mph		0	

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK										
Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.–Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	654	1,312	0	1,966	94,010	2.1	2,244	0	17,554	6.0
O'Hare/Logan Square	1,989	1,418	4,984	8,391	152,956	5.5	4,322	0		
Dearborn Subway	7,197	0	0	7,197	45,818	15.6	4,938	0		
North Main Line	4,092	4,286	1,625	10,003	78,966	12.7	0	0	19,895	8.6
State Subway	1,032	0	0	1,032	51,328	2.0	644	0		
Dan Ryan	1,517	3,079	4,264	8,860	101,332	8.7	0	0		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	6,642	1,519	8,161	40,714	20.0	0	0	32,110	31.6
Evanston Express	3,675	10,919	9,355	23,949	60,970	39.3	0	0		
Loop	0	0	0	0	21,470	0	0	0	0	0
Ravenswood/Ravenswood–Loop	1,481	0	0	1,481	98,364	1.5	0	0	1,481	1.5
Midway/Grand Junction	1,877	251	0	2,128	99,224	2.1	0	0	2,128	2.1
Lake	0	0	0	0	93,114	0	0	0	12,231	5.9
South Loop/South Main Line	629	1,005	1,250	2,884	68,906	4.2	0	0		
Englewood	2,426	5,579	1,342	9,347	31,916	29.3	0	0		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	0	0	0	0	77,710	0	0	0	0	0
TOTALS	26,569	34,491	24,339	85,399	1,181,106	7.2	12,148	0		

NOT TO SCALE
GRAPHICAL REPRESENTATION

DATE	DESCRIPTION	
		IN CHARGE C.B.
		APPROVED BY B.M.jr
		CHECKED BY B.M.jr
		UPDATED BY S.M.
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.
		Prepared by: Track Maintenance

CTA RAIL CUSTOMER IMPACT MAP

November 25 , 2009
